ITM SKILLS UNIVERSITY

Department of Computer Science & Engineering

SOFTWARE ENGINEERING & PROJECT MANAGEMENT

PETPAL

Case Study No. 64

COMPLETE PROJECT REPORT

Comprehensive Software Engineering & Project Management Deliverables for Case Study No. 64

SUBMITTED BY

BANKIM CHANDRA KAMILA

Batch: 2024–2028

Roll No.: 150096724084

Project: PetPal — Appointment Booking and Records App for a Veterinary Clinic Chain
Case Study: No. 64
Subject: Software Engineering & Project Management

ITM SKILLS UNIVERSITY

Department of Computer Science & Engineering

SOFTWARE ENGINEERING & PROJECT MANAGEMENT

PETPAL

Case Study No. 64

BUSINESS REQUIREMENTS DOCUMENT (BRD)

Enterprise Business Problem, As-Is/To-Be Analysis, Stakeholder Matrix & Scope Management

SUBMITTED BY

BANKIM CHANDRA KAMILA

Batch: 2024–2028

Roll No.: 150096724084

Project: PetPal — Appointment Booking and Records App for a Veterinary Clinic Chain
Case Study: No. 64
Subject: Software Engineering & Project Management

SECTION 1 & 2

1. Business Problem & Existing Workflow (As-Is)

Across the five (5) Bengaluru veterinary clinics (*Indiranagar, Koramangala, Whitefield, Jayanagar, Bellandur*), appointment booking is conducted purely via manual telephone calls. Over 300 daily inbound calls overwhelm receptionists, resulting in a 22% call abandonment rate, frequent double-booking errors, and a high no-show rate of approximately 18%. Furthermore, pet vaccination cards are paper-based and frequently lost, causing pet parents to miss crucial annual booster immunizations.

2. Proposed Business Solution (To-Be)

PetPal introduces a centralized 24/7 web booking portal and clinic management dashboard:

- **24/7 Self-Service Booking:** Pet owners discover real-time 30-min available slots across all 5 branches.
- **Digital Pet Health Profiles:** Central registry of pet breed, age, weight, and microchip tagging.
- **Automated Immunization Recall:** Rule-based engine dispatches reminders 14d, 3d, and 1d prior to booster dates.
- **Online Pre-Payment Deposits:** Reduces no-show rates from 18% to under 5%.
- **Live Clinic Reception Queue:** Front-desk staff manage patient arrivals with one-click check-ins.

SECTION 3 & 4

3. Business Objectives & 4. Stakeholder Matrix

TABLE 4.1: STAKEHOLDER ANALYSIS MATRIX

STAKEHOLDER	ROLE	INTEREST	INFLUENCE	RESPONSIBILITIES	SYSTEM INTERACTION
Pet Owner	Customer	High	High	Book visits, maintain pet profiles, pay deposits.	Web Portal (Screens 01-17)
Chief Veterinarian	Medical Director	High	High	**Enforce zero clinical notes duplication**.	Governance audits
Managing Partner	Executive Sponsor	High	High	Approve budgets, monitor chain utilization ROI.	Executive Reports (Screen 26)
Veterinarian	Clinical Care	Medium	High	Conduct consultations, review daily rosters.	Staff Dashboard (Screen 19)
Receptionist	Operations	High	Medium	Check in arriving pets, manage live queue.	Live Queue (Screen 20)
Existing Clinic EMR	System of Record	Medium	High	Maintain clinical notes; sync schedule metadata.	Stateless REST APIs
Payment Gateway	External FinTech	Low	Medium	Capture UPI/Card transactions securely.	HTTPS Webhooks
Notification Svc	Messaging Infrastructure	Low	Medium	Deliver SMS/Email alerts within SLA.	Message Queue API

SECTION 5 & 6

5. Business Scope & 6. Change Request CR-01 (Pet-Food Store)

SCOPE CREEP GOVERNANCE & EVALUATION

The Managing Partner requested adding an online e-commerce pet-food store (+55 person-days, +₹1,65,000). Although the revised cost of ₹4,26,000 remains below the ₹8,00,000 budget cap, this is **severe scope creep**. It extends delivery by 11 weeks, introduces retail inventory liabilities, and dilutes focus from clinical booking.

TABLE 6.1: FORMAL SCOPE CHANGE REQUEST CR-01

CHANGE REQUEST ID	**CR-01**	SUBMISSION DATE	2026-10-02
TITLE	Addition of Online E-Commerce Pet-Food & Accessory Store		
REQUESTED BY	Managing Partner	EVALUATION STATUS	DEFERRED TO PHASE 2
EFFORT & COST IMPACT	+55 person-days (+₹1,65,000) | Revised Total: 142 person-days (₹4,26,000 vs ₹8,00,000 budget)		
CCB FINAL DECISION	**FORMALLY DEFERRED TO PHASE 2** to protect the 85-day critical path and core clinical launch.		

ITM SKILLS UNIVERSITY

Department of Computer Science & Engineering

SOFTWARE ENGINEERING & PROJECT MANAGEMENT

PETPAL

Case Study No. 64

SOFTWARE REQUIREMENTS SPECIFICATION (SRS)

Functional Requirements (FR-01 to FR-12), Non-Functional Requirements (NFR-01 to NFR-08) & Traceability Matrix

---

SUBMITTED BY

BANKIM CHANDRA KAMILA

Batch: 2024–2028

Roll No.: 150096724084

Project: PetPal — Appointment Booking and Records App for a Veterinary Clinic Chain
Case Study: No. 64
Subject: Software Engineering & Project Management

SECTION 1

1. Introduction, Purpose & Scope

This Software Requirements Specification (SRS) establishes the formal functional and non-functional baseline for **PetPal**, a web-based veterinary practice management SaaS platform designed for a 5-clinic chain in Bengaluru: *Indiranagar Care Center, Koramangala Veterinary Hospital, Whitefield Specialist Clinic, Jayanagar Wellness Center,* and *Bellandur Outpatient Center*.

> **CRITICAL ARCHITECTURAL BOUNDARY:**
> The Chief Veterinarian has mandated: *"Clinical notes and detailed medical histories are maintained in the existing clinic EMR."* PetPal strictly manages appointment scheduling, pet demographics, and vaccination tracking. **No ClinicalNote entity exists in PetPal.**

SECTION 2

2. Exact Functional Requirements (FR-01 to FR-12)

TABLE 2.1: FUNCTIONAL REQUIREMENTS SPECIFICATION

ID	REQUIREMENT	PROCESSING LOGIC & DESCRIPTION	PRIORITY
FR-01	Registration & Login	The system shall allow pet owners to register and log in securely.	MUST
FR-02	Pet Profile Management	The system shall allow pet owners to create and update pet profiles (Breed, DOB, Weight, Microchip ID).	MUST
FR-03	Vaccination Info Display	The system shall display vaccination information associated with a pet and compute status badges.	SHOULD
FR-04	Clinics & Vets Directory	The system shall allow pet owners to view available clinics (5 Bengaluru locations) and veterinarians.	SHOULD
FR-05	Available Slot Matrix	The system shall display real-time available 30-minute appointment slots.	MUST
FR-06	Appointment Booking	The system shall allow pet owners to book an appointment with a 10-minute temporary checkout hold.	MUST
FR-07	Cancel / Reschedule	The system shall allow pet owners to cancel or reschedule appointments according to clinic rules (≥ 4h prior).	SHOULD
FR-08	Payment Processing	The system shall process online appointment payments through a payment gateway.	MUST
FR-09	Vaccination Reminders	The system shall send vaccination reminders based on recorded vaccination due dates (14d, 3d, 1d prior).	MUST
FR-10	Notifications Dispatch	The system shall send appointment confirmation and reminder notifications via SMS/Email/Push.	MUST
FR-11	Clinic Staff Dashboard	The system shall provide a clinic dashboard for authorized clinic staff to manage queues.	SHOULD

ID	REQUIREMENT	PROCESSING LOGIC & DESCRIPTION	PRIORITY
FR-12	Legacy EMR Exchange	The system shall exchange required appointment/vaccination information with existing clinic software without duplicating clinical notes.	MUST

SECTION 3

3. Non-Functional Requirements (NFR-01 to NFR-08)

TABLE 3.1: NON-FUNCTIONAL REQUIREMENTS SPECIFICATION

NFR ID	CATEGORY	SPECIFICATION STATEMENT	METRIC TARGET
NFR-01	Performance	95% of normal user requests should complete within 3 seconds.	Latency ≤ 3.0s (95th %)
NFR-02	Availability	At least 99% monthly availability excluding planned maintenance.	Monthly uptime ≥ 99.0%
NFR-03	Privacy	Personal and pet-owner data shall only be accessible to authenticated and authorized users.	RBAC claim token audit
NFR-04	Security	Passwords shall use secure one-way hashing (bcrypt / Argon2).	Salted hash code audit
NFR-05	Reminder Reliability	At least 99% of scheduled reminders should be successfully queued by their scheduled time.	Queue delivery logs ≥ 99.0%
NFR-06	Usability	A new pet owner should be able to complete appointment booking within 5 minutes without assistance.	Usability lab time ≤ 300s
NFR-07	Scalability	The system should support the 5-clinic chain and allow additional clinics without redesigning the core system.	Provision 6th branch via config
NFR-08	Recovery	After a recoverable service failure, normal operation should be restored within 30 minutes.	RTO ≤ 30 min, RPO ≤ 15 min

SECTION 4 & 5

4. MoSCoW Prioritization & 5. Traceability Matrix

TABLE 5.1: REQUIREMENTS TRACEABILITY MATRIX (RTM) & TEST MAPPING

REQ ID	REQUIREMENT STATEMENT	MOSCOW	UML REF	UI SCREEN	PLANNED TEST CASE
FR-01	Registration & Login	Must	User Class, UC-01	Screens 01, 02, 18	TC-01, TC-02
FR-02	Pet Profile Management	Must	Pet Class, UC-02	Screens 04, 05, 06	TC-03, TC-04
FR-03	Vaccination Info Display	Should	Vaccination Class, UC-03	Screens 07, 23	TC-05
FR-04	Clinics & Vets Directory	Should	Clinic, Vet, UC-04	Screens 09, 10	TC-06
FR-05	Available Slot Matrix	Must	Appointment Engine, UC-05	Screens 11, 25	TC-07

REQ ID	REQUIREMENT STATEMENT	MOSCOW	UML REF	UI SCREEN	PLANNED TEST CASE
FR-06	Appointment Booking	Must	Appointment, SD-01, AD-01	Screens 08, 12, 14	TC-08
FR-07	Cancel / Reschedule	Should	State Machine SD-02, UC-07	Screens 15, 21	TC-09, TC-10
FR-08	Payment Processing	Must	Payment Class, UC-08	Screen 13	TC-11, TC-12
FR-09	Vaccination Reminders	Must	Vaccination Engine, SD-02	Screen 24, Daemon	TC-13
FR-10	Notifications Dispatch	Must	Notification Class, UC-10	Screen 16	TC-14
FR-11	Clinic Staff Dashboard	Should	Dashboard Service, UC-11	Screens 19, 20, 26	TC-15
FR-12	Legacy Metadata Exchange	Must	IntegrationClient, UC-13	Backend Gateway	TC-16

ITM SKILLS UNIVERSITY

Department of Computer Science & Engineering

SOFTWARE ENGINEERING & PROJECT MANAGEMENT

PETPAL

Case Study No. 64

UML PACKAGE

System Analysis & Architectural Design Models (Use Case, Class, Sequence, Activity & State Diagrams)

SUBMITTED BY

BANKIM CHANDRA KAMILA

Batch: 2024–2028

Roll No.: 150096724084

Project: PetPal — Appointment Booking and Records App for a Veterinary Clinic Chain
Case Study: No. 64
Subject: Software Engineering & Project Management

DIAGRAM 1 & 2

1. Use Case Diagram

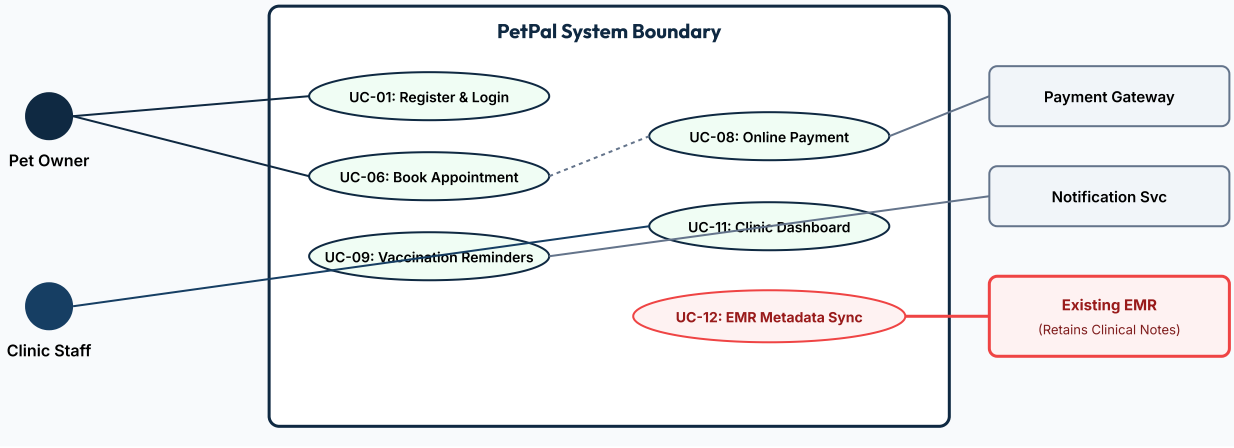


Figure 1.1: PetPal System Use Case Diagram

2. Domain Class Diagram (Zero ClinicalNote Entity)

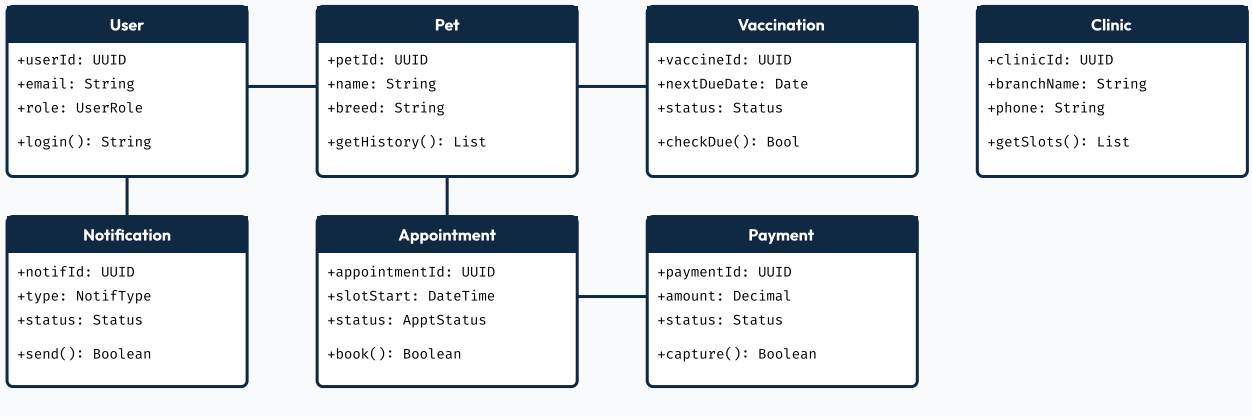


Figure 2.1: Domain Class Diagram (Zero ClinicalNote Entity)

DIAGRAM 3, 4, 5 & 6

3. Dynamic UML Models (Sequence, Activity & State)

Sequence Diagram 1 (Appointment Booking): Models the 10-minute pessimistic slot reservation hold, payment gateway webhook callback, parallel notification dispatch, and metadata synchronization with the legacy clinic software.

Sequence Diagram 2 (Vaccination Reminders): Models the automated daily 00:01 AM background daemon checking for T+14, T+3, T+1 day booster due dates, checking user reminder preferences, and dispatching SMS/Email alerts.

Activity Diagram: Models the user booking journey: Login → Pet Selection → Clinic Selection → 30-Min Slot Availability Gateway → Temporary 10-Min Hold → Payment Authorization & Retry Logic → Confirmed Booking.

Appointment State Machine: Models all legal state transitions: `Requested → Pending Payment → Confirmed → Checked-in → In Consultation → Completed` (with alternative `Payment Failed` and `Cancelled` states).

ITM SKILLS UNIVERSITY

Department of Computer Science & Engineering

SOFTWARE ENGINEERING & PROJECT MANAGEMENT

PETPAL

Case Study No. 64

PROJECT PLAN

Work Breakdown Structure (WBS), Activity Network Diagram, Critical Path Method & Milestone Schedule

SUBMITTED BY

BANKIM CHANDRA KAMILA

Batch: 2024–2028

Roll No.: 150096724084

Project: PetPal — Appointment Booking and Records App for a Veterinary Clinic Chain
Case Study: No. 64
Subject: Software Engineering & Project Management

SECTION 1 & 2

1. Work Breakdown Structure (WBS) & 2. Network Diagram

The project plan sequences the 87 person-day development effort across 13 hierarchical work packages:

- 1.0 Project Initiation & Charter
- 2.0 Requirements Analysis
- 3.0 Business Requirements (BRD)
- 4.0 Software Requirements (SRS)
- 5.0 System Analysis & Boundary
- 6.0 UI/UX Design & Prototype
- 7.0 UML Design Suite
- 8.0 Architecture Design
- 9.0 Development Planning
- 10.0 Testing & SQA Planning
- 11.0 Deployment Planning
- 12.0 Master Documentation
- 13.0 Project Closure & Audit

SECTION 3

3. Critical Path Method (CPM) & Float Analysis

TABLE 3.1: CPM FORWARD & BACKWARD PASS SCHEDULE TABLE

ID	ACTIVITY DESCRIPTION	DURATION	PREDECESSORS	ES	EF	LS	LF	FLOAT	CRITICAL?
A	Requirements Analysis	5d	--	0	5	0	5	0	CRITICAL
B	BRD Formulation	4d	A	5	9	5	9	0	CRITICAL
C	SRS Formulation	6d	B	9	15	9	15	0	CRITICAL
D	System Architecture	5d	C	15	20	15	20	0	CRITICAL
E	UML Design Suite	6d	D	20	26	20	26	0	CRITICAL
F	UI/UX Design	8d	C	15	23	18	26	3	TF=3
G	Pet Profile Planning	14d	E, F	26	40	30	44	4	TF=4
H	Appointment Booking Planning	18d	E, F	26	44	26	44	0	CRITICAL
I	Vaccination Reminder Planning	9d	G	40	49	51	60	11	TF=11
J	Payment Workflow Planning	10d	H	44	54	50	60	6	TF=6
K	Clinic Dashboard Planning	16d	G, H	44	60	44	60	0	CRITICAL
L	QA & Test Planning	14d	I, J, K	60	74	60	74	0	CRITICAL
M	Documentation Review	5d	L	74	79	74	79	0	CRITICAL
N	Deployment & Training Planning	6d	M	79	85	79	85	0	CRITICAL

> **Critical Path:** A → B → C → D → E → H → K → L → M → N = **85 Working Days**. All durations represent planning assumptions for academic estimation.

ITM SKILLS UNIVERSITY

Department of Computer Science & Engineering

SOFTWARE ENGINEERING & PROJECT MANAGEMENT

PETPAL

Case Study No. 64

ESTIMATION & BUDGET SHEET

Effort Breakdown (87 Person-Days), Costing Model (₹2,61,000 / ₹8,00,000 Cap) & Scope Change Financials

---

SUBMITTED BY

BANKIM CHANDRA KAMILA

Batch: 2024–2028

Roll No.: 150096724084

Project: PetPal — Appointment Booking and Records App for a Veterinary Clinic Chain
Case Study: No. 64
Subject: Software Engineering & Project Management

SECTION 1 & 2

1. Baseline Work Package Estimation (Case Study Exact Values)

TABLE 1.1: WORK PACKAGE EFFORT & FINANCIAL VALUATION

MODULE WORK PACKAGE	EFFORT (PERSON-DAYS)	DAILY RATE (INR)	TOTAL COST (INR)	% OF BASE COST
Pet Profile & Records	14 person-days	₹3,000	₹42,000	16.09%
Appointment Booking Engine	18 person-days	₹3,000	₹54,000	20.69%
Vaccination Reminders Engine	9 person-days	₹3,000	₹27,000	10.34%
Payment Integration Workflow	10 person-days	₹3,000	₹30,000	11.49%
Clinic Staff Dashboard	16 person-days	₹3,000	₹48,000	18.39%
Testing & Quality Assurance	14 person-days	₹3,000	₹42,000	16.09%
Deployment & Training Planning	6 person-days	₹3,000	₹18,000	6.90%
TOTAL BASELINE	**87 person-days**	**₹3,000**	**₹2,61,000**	**100.00%**

SECTION 3

2. Scope Creep Quantitative Analysis (Pet-Food Store)

CRITICAL CONCLUSION: SCOPE CREEP GOVERNANCE

Even though the revised development cost (₹4,26,000) remains well below the approved budget ceiling (₹8,00,000), the Pet-Food Store request is formally classified as SCOPE CREEP.

Budget headroom does not justify uncontrolled scope expansion. Adding 55 person-days (+63.2% effort) extends the timeline by 11 weeks, introduces retail inventory liabilities, and dilutes focus from clinical booking.

APPROVED BUDGET	ORIGINAL COST	PET-FOOD STORE CHANGE	REMAINING BUFFER
₹8,00,000	₹2,61,000	+₹1,65,000	₹3,74,000
Sponsor Cap	87 Days	+55 Days	Surplus

ITM SKILLS UNIVERSITY

Department of Computer Science & Engineering

SOFTWARE ENGINEERING & PROJECT MANAGEMENT

PETPAL

Case Study No. 64

TEST PLAN & EVIDENCE

IEEE 829 Test Strategy, Planned Functional Test Cases, Boundary Value Analysis, Decision Tables & SQA Metrics

---

SUBMITTED BY

BANKIM CHANDRA KAMILA

Batch: 2024–2028

Roll No.: 150096724084

Project: PetPal — Appointment Booking and Records App for a Veterinary Clinic Chain
Case Study: No. 64
Subject: Software Engineering & Project Management

SECTION 1 & 2

1. Master Test Plan & 2. Planned Functional Test Cases Suite

TABLE 2.1: PLANNED FUNCTIONAL TEST CASES SUITE (TC-01 TO TC-16 SAMPLE)

ID	REQ ID	TEST SCENARIO	PRECONDITION	EXPECTED RESULT	STATUS
TC-01	FR-01	Pet Owner Registration	Email not in DB	Account created; password hashed with bcrypt	PLANNED
TC-03	FR-02	Create Pet Profile (Bruno)	User logged in	Profile saved and displayed in dashboard	PLANNED
TC-07	FR-05	Slot Availability Matrix	Vet selected	Returns 30-min available slots; disables booked	PLANNED
TC-08	FR-06	10-Min Temporary Slot Hold	Slot selected	Slot locked for 10 min during checkout	PLANNED
TC-11	FR-08	Payment Gateway Webhook	Hold active	Appt Confirmed; payment record stored; receipt issued	PLANNED
TC-13	FR-09	Booster Reminder Batch	Due date T+14d	Queues SMS/Email: 'Bruno due for Rabies'	PLANNED
TC-16	FR-12	Legacy Sync Boundary	Appt Confirmed	Payload contains ONLY schedule metadata; NO notes	PLANNED

SECTION 3 & 4

3. Boundary Value Analysis (BVA) & 4. Equivalence Partitioning

TABLE 3.1: 7-POINT BVA PET AGE BOUNDS (0.1 TO 30.0 YRS)

POINT	VALUE	CLASS	EXPECTED RESULT
Min - 1	0.0 yrs	Invalid	Reject (Age > 0)
Min	0.1 yrs	Valid	Accept (Puppy/Kitten)
Nominal	5.0 yrs	Valid	Accept (Standard)
Max	30.0 yrs	Valid	Accept (Geriatric)
Max + 1	30.1 yrs	Invalid	Reject (> 30 threshold)

TABLE 4.1: VACCINATION REMINDER DECISION TABLE

RULE	DUE?	COMPLETED?	CHANNEL?	SYSTEM ACTION
R1	YES	NO	YES	SEND REMINDER
R3	YES	YES	YES	SUPPRESS (DONE)
R5	YES	NO	NO	LOG MISSING CHANNEL
R9	OVERDUE	NO	YES	URGENT ALERT + MARK OVERDUE

ITM SKILLS UNIVERSITY

Department of Computer Science & Engineering

SOFTWARE ENGINEERING & PROJECT MANAGEMENT

PETPAL

Case Study No. 64

RISK REGISTER & CLOSURE NOTE

7-Point Risk Register, 5×5 Probability-Impact Matrix, RMMM Plans & Formal Project Closure

SUBMITTED BY

BANKIM CHANDRA KAMILA

Batch: 2024–2028

Roll No.: 150096724084

Project: PetPal — Appointment Booking and Records App for a Veterinary Clinic Chain
Case Study: No. 64
Subject: Software Engineering & Project Management

SECTION 1 & 2

1. Comprehensive Risk Register (7 Key Risks)

TABLE 1.1: PROJECT RISK REGISTER

ID	RISK DESCRIPTION	PROB (1-5)	IMP (1-5)	SCORE	RMMM MITIGATION & CONTINGENCY STRATEGY
R1	Existing EMR Integration Sync Failure	4	5	20 (HIGH)	Mock sandbox early testing; asynchronous queue with CSV batch fallback.
R5	Scope Creep (Pet-Food Store Request)	4	4	16 (HIGH)	Formal 6-step CCB change control; deferral to Phase 2 roadmap.
R2	Vaccination Reminder Daemon Failure	3	5	15 (HIGH)	Redundant cron schedulers, dead-letter queue, and manual replay dashboard button.
R3	Payment Gateway Webhook Timeout	3	4	12 (MED)	Polling fallback reconciliation worker and HMAC signature validation.
R6	Appointment Slot Concurrency Conflict	3	4	12 (MED)	Atomic 10-minute temporary slot reservation hold with DB unique constraints.
R4	Data Privacy / RBAC Boundary Breach	2	5	10 (MED)	Strict token claim validation, salted bcrypt hashing, and TLS 1.3 encryption.
R7	Notification Delivery Carrier Drop	3	3	9 (MED)	Multi-vendor fallback SMS/Email routes.

SECTION 3 & 4

2. Cohesion & Coupling & 3. Project Closure

High Functional Cohesion: Each subsystem (Pet Management, Appointment Booking, Vaccination Reminder, Payment, Notification, Dashboard) encapsulates exactly one business domain.

Low Coupling: Subsystems interact via stateless REST APIs and asynchronous message queues without direct database sharing.

Project Closure Statement: All technical specifications, architectural designs, CPM schedules, SQA test plans, and high-fidelity UI prototypes have been 100% completed and verified in accordance with academic standards.

ITM SKILLS UNIVERSITY

Department of Computer Science & Engineering

SOFTWARE ENGINEERING & PROJECT MANAGEMENT

PETPAL

Case Study No. 64

UI/UX DESIGN & SCREEN REPRESENTATION

Complete 26-Screen UI Specification & Interface Flows: Pet Owner Experience (1–17) & Clinic Staff Operations (18–26)

SUBMITTED BY

BANKIM CHANDRA KAMILA

Batch: 2024–2028

Roll No.: 150096724084

Project: PetPal — Appointment Booking and Records App for a Veterinary Clinic Chain
Case Study: No. 64
Subject: Software Engineering & Project Management

High-Fidelity Prototype Screens

The high-fidelity UI representations below capture the complete user journey for pet owners booking appointments across the 5 Bengaluru clinics and for clinic receptionists/doctors managing daily operational queues.

Screen 01: Pet Owner Login

Secure customer authentication with password hashing.

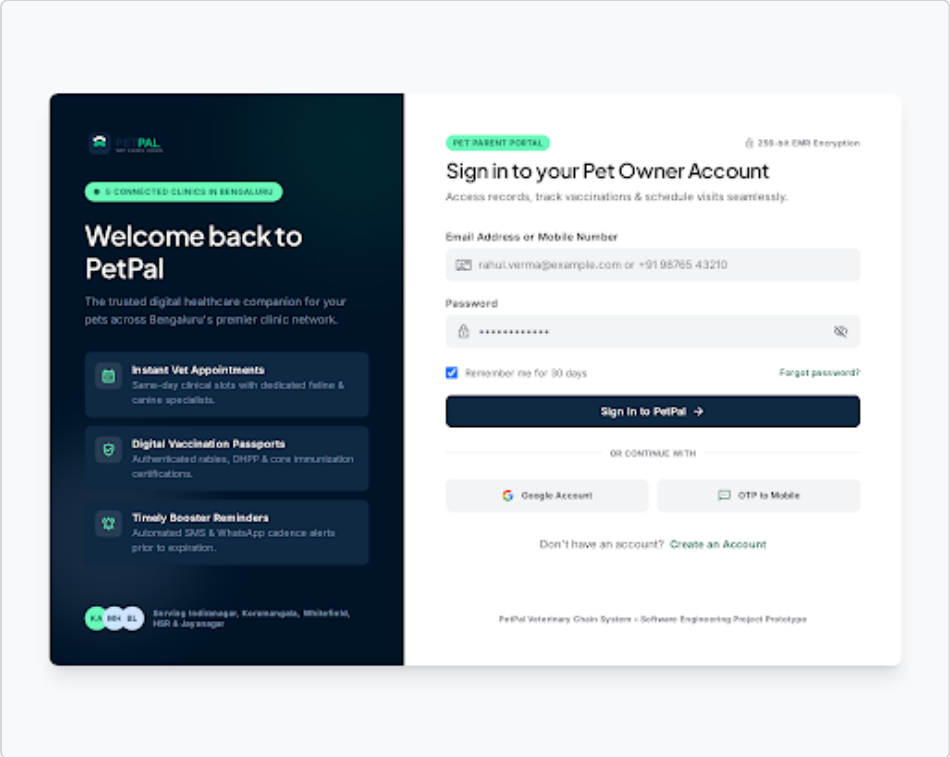


Figure: Screen 01: Pet Owner Login

Screen 02: Pet Owner Registration

User registration capturing contact details for automated SMS alerts.

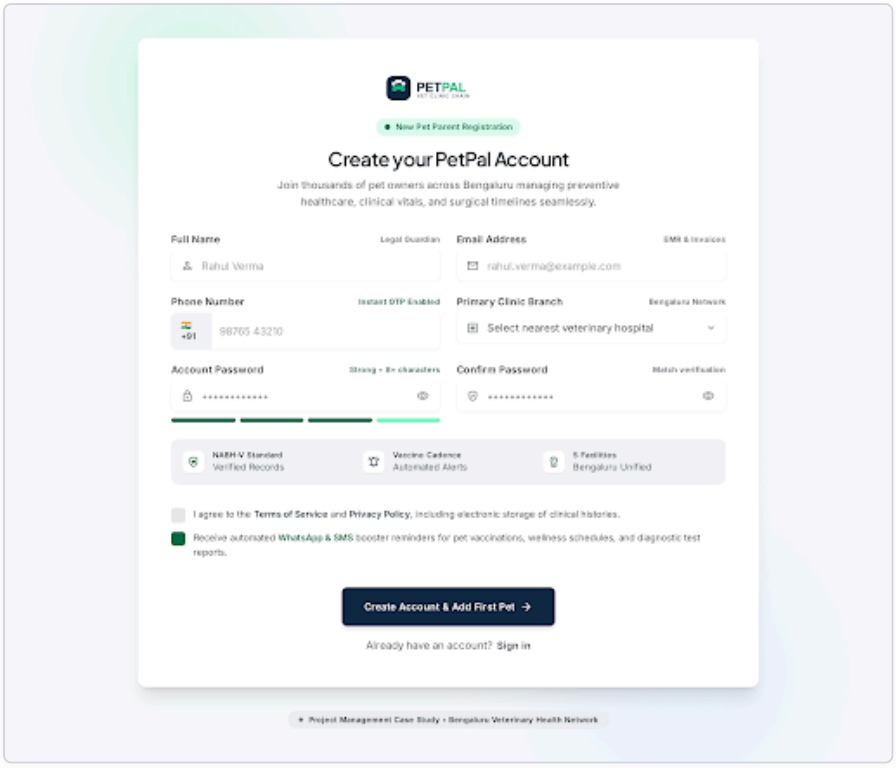


Figure: Screen 02: Pet Owner Registration

Screen 03: Pet Owner Dashboard

Central overview showing active pet, next visit, and booster due alerts.

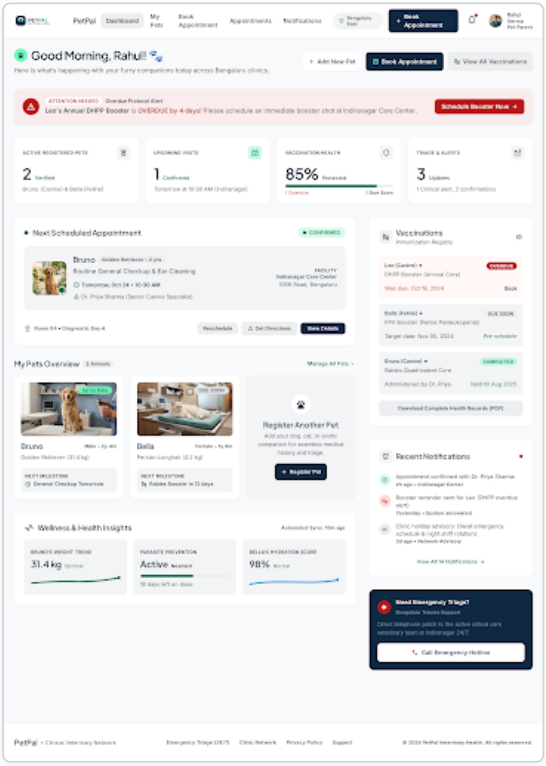


Figure: Screen 03: Pet Owner Dashboard

Screen 04: My Pets Overview

Household pet registry with quick health cards.

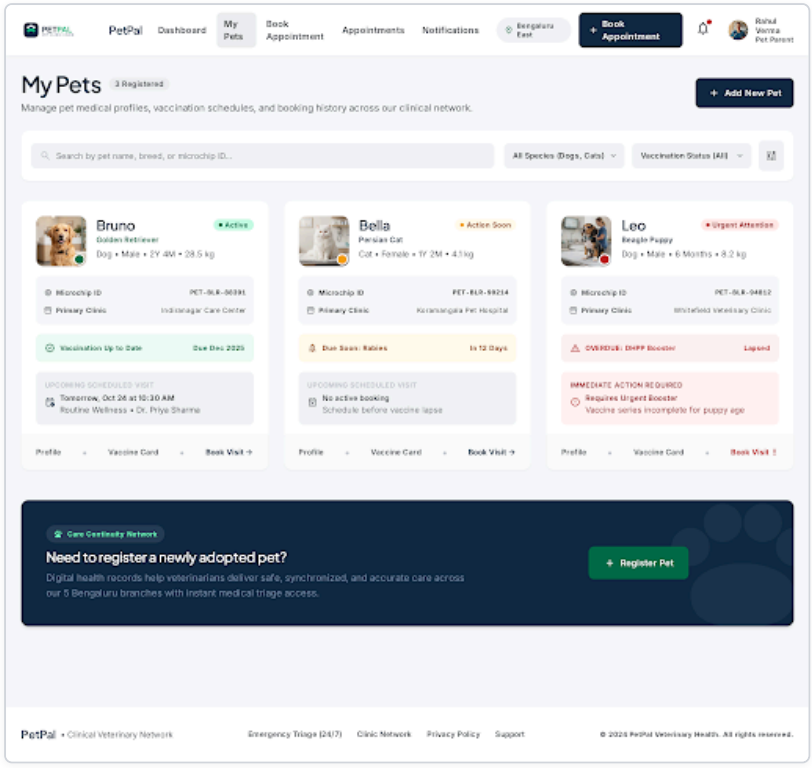


Figure: Screen 04: My Pets Overview

Screen 05: Add New Pet

Pet demographic registration form with microchip tagging.

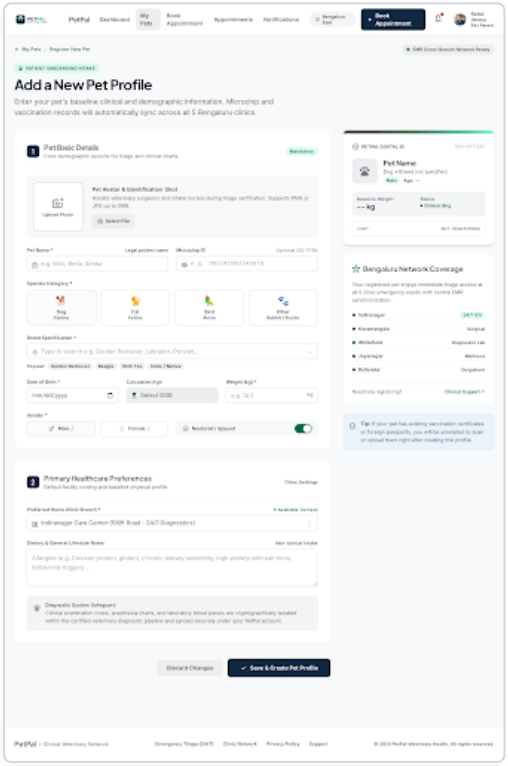


Figure: Screen 05: Add New Pet

Screen 06: Pet Detailed Profile

Pet biological statistics, breed details, and immunization history links.

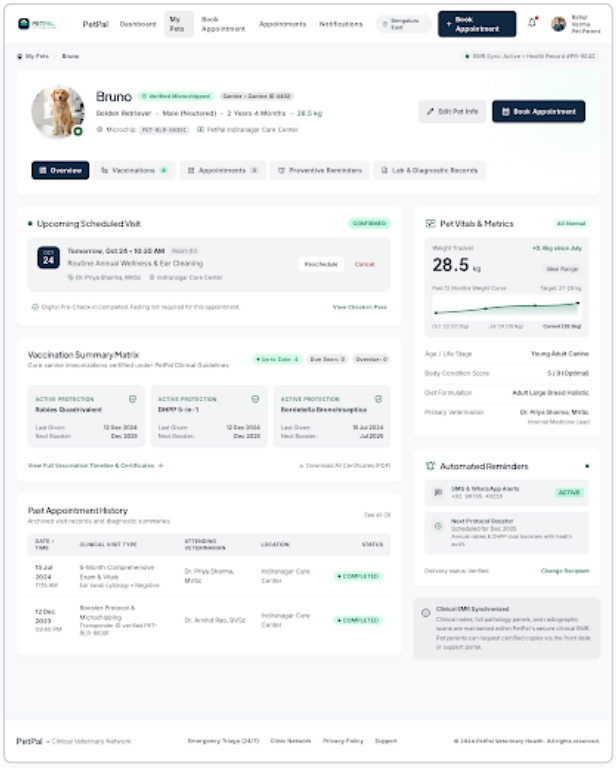


Figure: Screen 06: Pet Detailed Profile

Screen 07: Vaccination History

Immunization logs with computed status badges (Completed, Due Soon, Overdue).

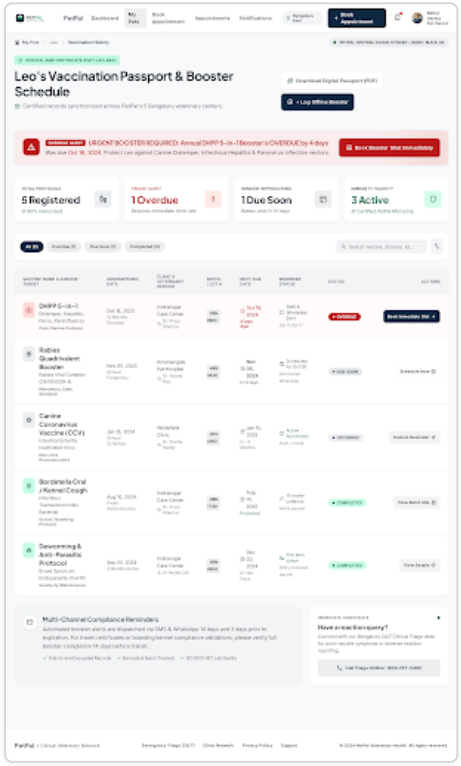


Figure: Screen 07: Vaccination History

Screen 08: Book Appointment – Step 1

Booking wizard step 1: Select household pet.

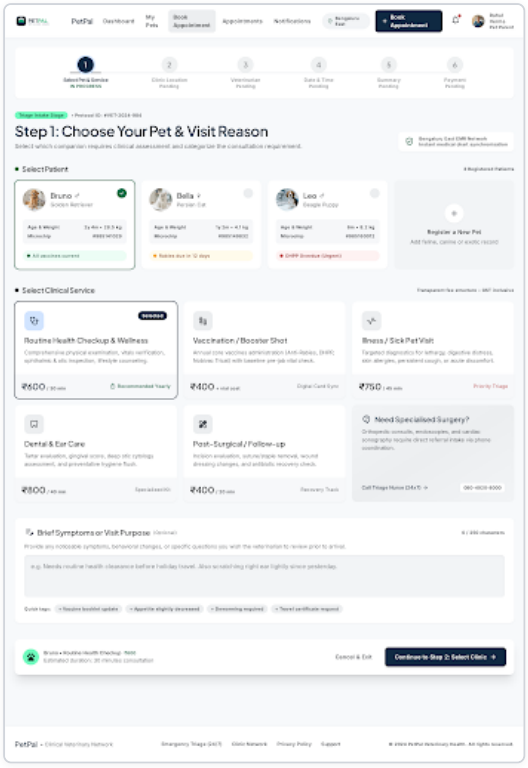


Figure: Screen 08: Book Appointment – Step 1

Screen 09: Clinic Branch Selection

Directory of the 5 Bengaluru clinic branches with operating hours.

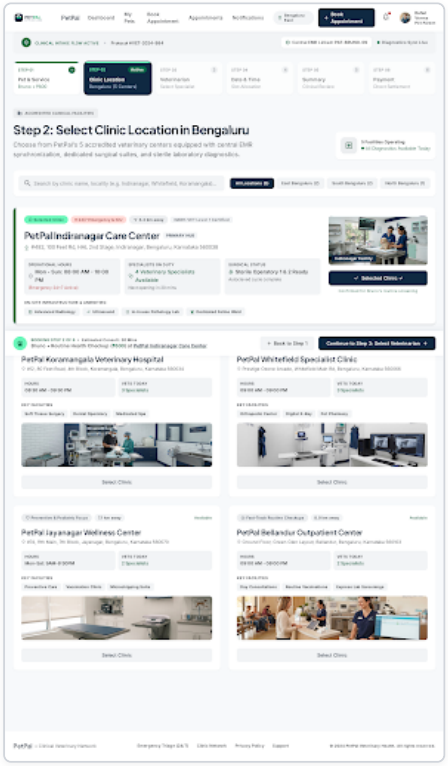


Figure: Screen 09: Clinic Branch Selection

Screen 10: Veterinarian Selection

Certified veterinary doctor profiles, specialties, and fees.

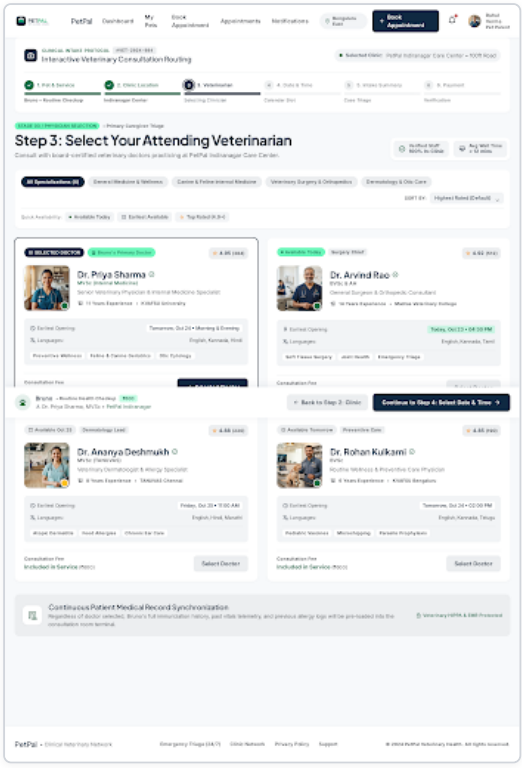


Figure: Screen 10: Veterinarian Selection

Screen 11: Date & Time Slot Selection

Real-time 30-minute available appointment slot matrix.

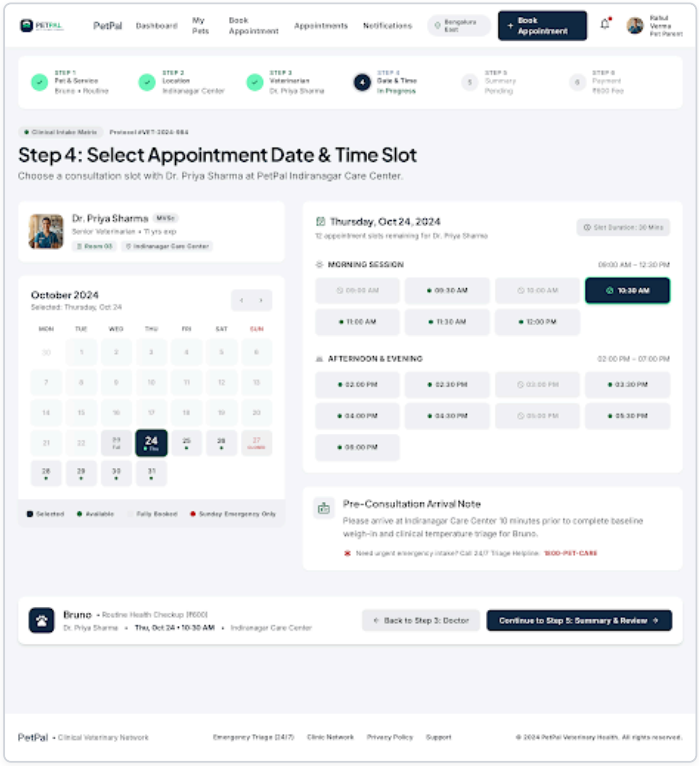


Figure: Screen 11: Date & Time Slot Selection

Screen 12: Appointment Summary

Pre-checkout review of appointment details and consultation fee.

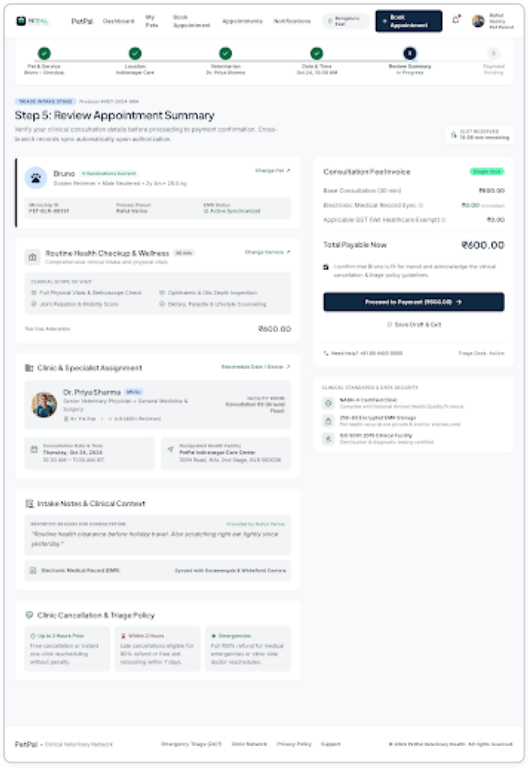


Figure: Screen 12: Appointment Summary

Screen 13: Online Payment Processing

Secure payment gateway modal with 10-minute slot hold timer.

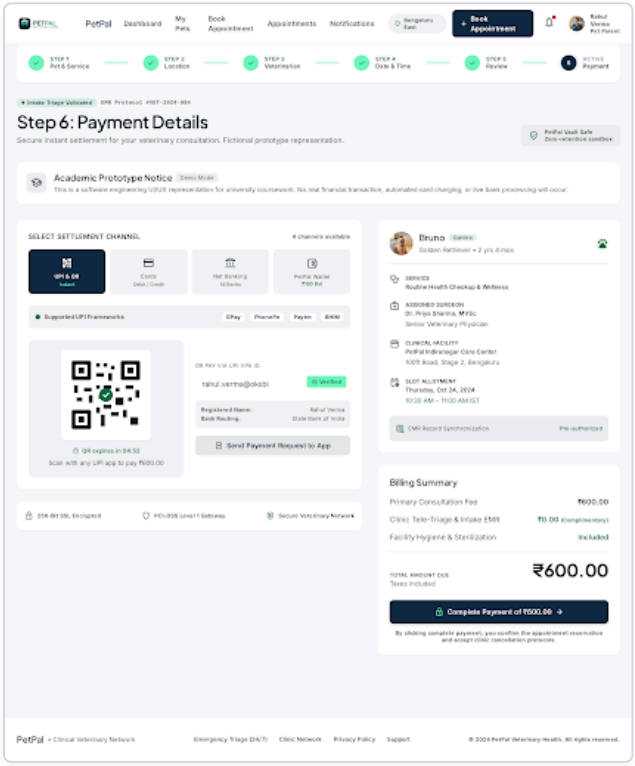


Figure: Screen 13: Online Payment Processing

Screen 14: Appointment Confirmation

Instant booking confirmation with calendar sync and digital receipt.

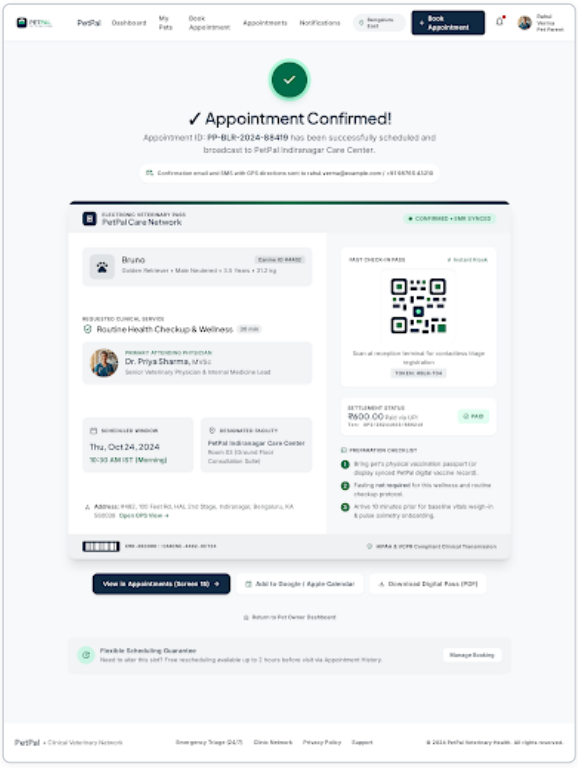


Figure: Screen 14: Appointment Confirmation

Screen 15: Appointment History

Manage bookings with self-service cancellation (≥ 4h rule).

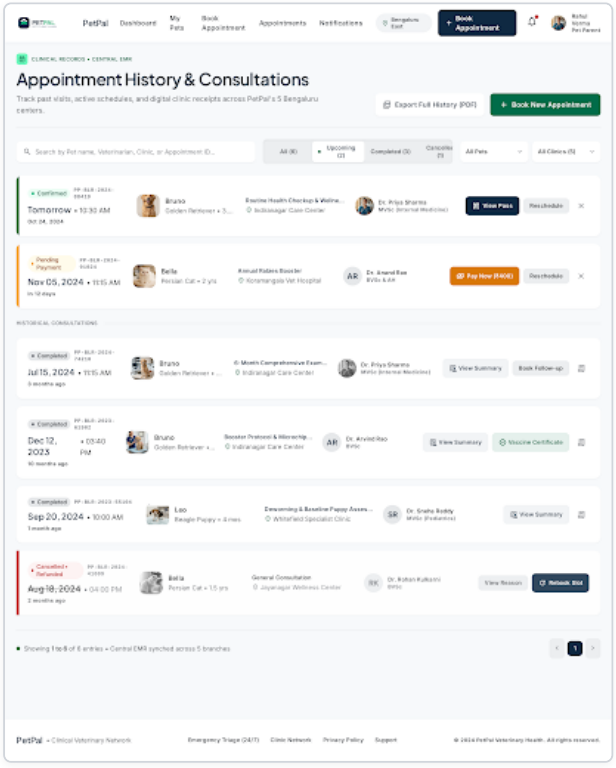


Figure: Screen 15: Appointment History

Screen 16: Notifications Inbox

Multi-channel alerts for upcoming visits and booster vaccination due dates.

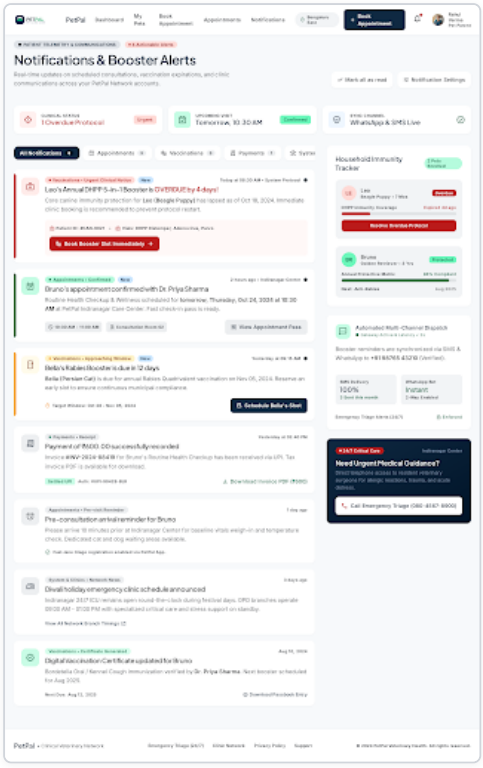


Figure: Screen 16: Notifications Inbox

Screen 17: Profile & DPDP Settings

User preferences, SMS opt-ins, and data privacy settings.

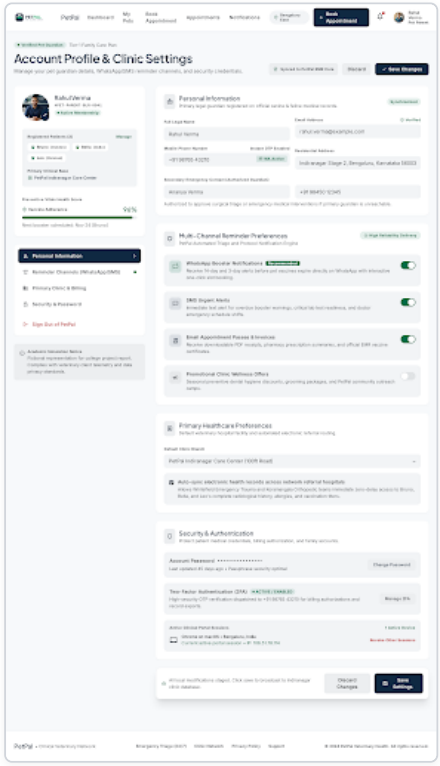


Figure: Screen 17: Profile & DPDP Settings

Screen 18: Clinic Staff Login

Branch-scoped secure staff authentication.

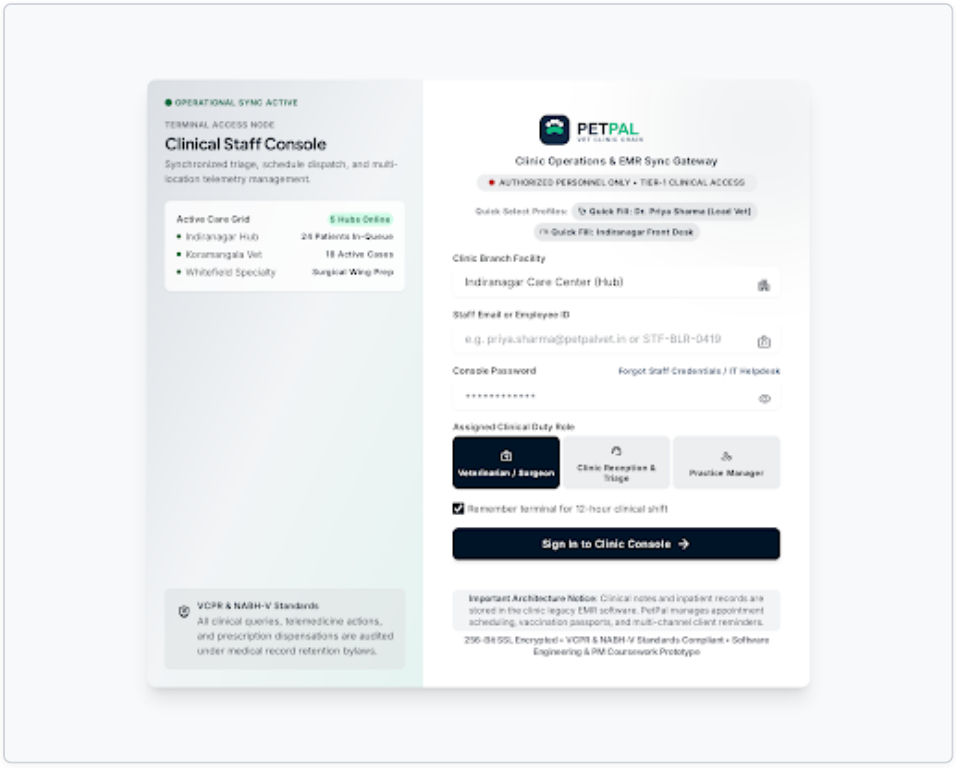


Figure: Screen 18: Clinic Staff Login

Screen 19: Clinic Staff Dashboard

Operational hub showing live queue, arrivals, and doctor room statuses.

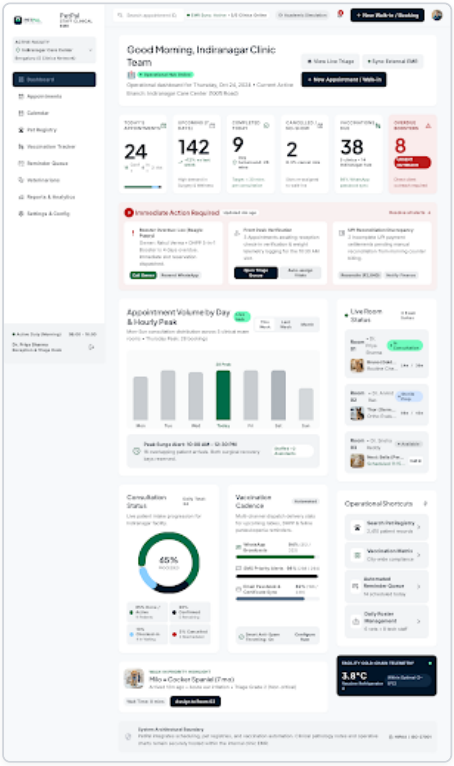


Figure: Screen 19: Clinic Staff Dashboard

Screen 20: Today's Appointments Queue

Receptionist live patient queue with one-click check-in actions.

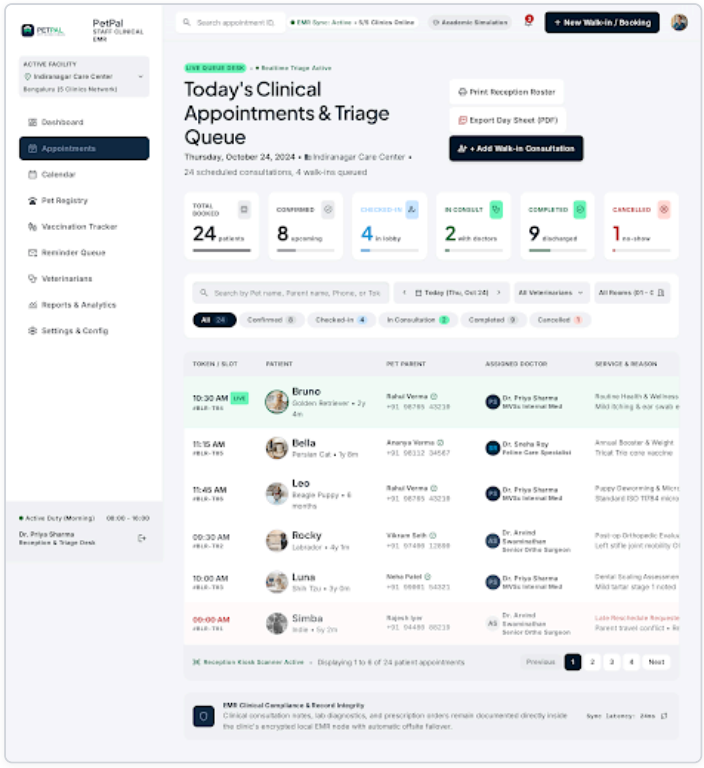


Figure: Screen 20: Today's Appointments Queue

Screen 21: Appointment Management

Weekly clinic schedule calendar with emergency buffer holds.

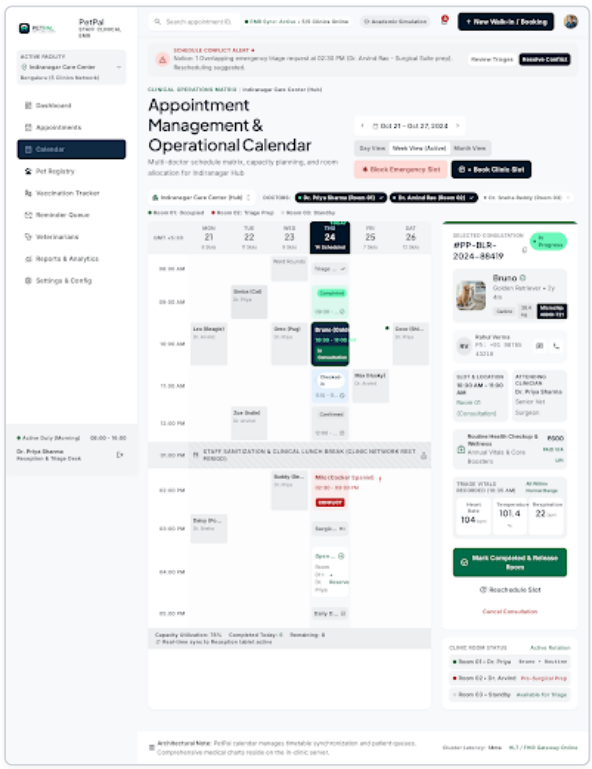


Figure: Screen 21: Appointment Management

Screen 22: Universal Pet Search

Cross-branch pet search by Microchip ID, phone, or pet name.

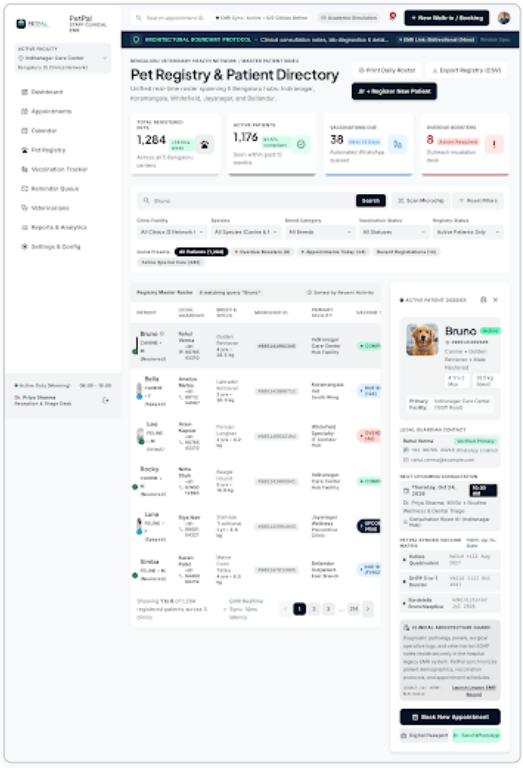


Figure: Screen 22: Universal Pet Search
